

PROJECT MANAGEMENT PLAN (PMP)

Project Name: Foresight — Digital Forensic Triage Suite

MASTER PROJECT CHARTER:

1. Executive Summary

Project Foresight is an automated digital forensics and incident triage web platform. It helps IT security teams quickly scan suspicious URLs, email headers, browser history, and files to detect cyber threats. The goal is to reduce incident analysis time from hours to minutes.

2. Core Business Objectives

- **Automation:** Automate 80% of repetitive evidence extraction tasks.
- **Accuracy:** Maintain high detection accuracy while minimizing false alerts.
- **Speed:** Process uploaded evidence files in under 30 seconds.

3. Key Scope & Core Deliverables

- **FastAPI Backend:** The core engine that processes uploaded evidence files and extracts metadata.
- **React Web Interface:** A dashboard for forensic analysts to upload files, view threat reports, and search historical data.
- **SQLite Evidence Vault:** A local database that securely stores evidence metadata and investigator audit logs.

4. Out of Scope

- Cloud-based multi-tenant SaaS architecture (V1 is single-organization / desktop-native web).
- Automated real-time network traffic interception.

5. Stakeholder Matrix

Stakeholder	Role	Primary Responsibility	Communication Frequency
Client Representative	Product Owner	Defines feature needs, approves milestones	Weekly Meeting & Email
IT Project Manager (You)	Project Lead	Manages budget, schedule, risks, and documentation	Daily Operations
Backend Engineer	Technical Lead	Builds FastAPI endpoints & extraction logic	Daily Stand-ups
Frontend Engineer	UI/UX Specialist	Builds React interface & accessibility features	Daily Stand-ups
QA Specialist	Tester	Runs validation test suites & false-positive checks	Weekly Sprint Demos

WORK BREAKDOWN STRUCTURE (WBS) & AGILE SPRINT ROADMAP:

Project Foresight

- └─ 1.0 Project Initiation & Discovery (Weeks 1-2)
- └─ 2.0 Backend Core Development (Weeks 3-6)
- └─ 3.0 Frontend UI Development (Weeks 5-8)
- └─ 4.0 Security & Audit Controls (Weeks 7-9)
- └─ 5.0 Testing, Quality Assurance & Tuning (Weeks 9-11)
- └─ 6.0 Client Handover & Deployment (Week 12)

Sprint	Phase Focus	Key Deliverables & Tasks	PM Milestone Checkpoint
Sprint 1	Requirement & Setup	Finalize requirements, design database schema, set up developer repositories.	Project Charter Sign-off
Sprint 2	Extraction Logic	Develop URL and Email header metadata extraction in FastAPI.	Backend Demo 1
Sprint 3	File & History Processing	Add File header parsing and Browser history file extraction capabilities.	Backend Demo 2
Sprint 4	Dashboard UI	Build React interface: file uploader, threat score badges,	Frontend Prototype Review

		search filters.	
Sprint 5	Vault & Access Control	Connect SQLite vault, implement investigator login, and build audit logging.	Full Integration Demo
Sprint 6	QA & Client Handover	Perform false-positive reduction testing, deliver client documentation, and deploy.	Final Client Acceptance

SPRINT BACKLOG & USER STORIES:

Risk ID	Risk Description	Likelihood	Impact	Mitigation Strategy (PM Action)
R-01	High false-positive rate flags harmless files as security threats.	High	High	Dedicate Sprint 5 to tuning accuracy scoring algorithms alongside client security experts.
R-02	Large forensic files cause browser or server timeouts.	Medium	High	Implement asynchronous file uploading and set a 50MB file size limit for V1.
R-03	Scope creep from client requesting cloud deployment mid-project.	High	Medium	Enforce strict change-control process: place new cloud requests into V2 backlog.
R-04	Developer missing technical context on forensic email parsing.	Medium	Medium	Provide open-source forensic library documentation and pair senior backend dev with QA.

SPRINT BACKLOG & USER STORIES:

The screenshot shows the Jira Project Foresight interface. The left sidebar contains navigation options: For you, Recent, Starred, Apps, Plans, Spaces, Recent, Project Foresight, AI Customer Support, More spaces, Recommended, Collect requests, Filters, Dashboards, Confluence, and Assets. The main content area displays the 'Project Foresight' space with a 'Backlog' view. A 'PF Sprint 1' is active, spanning from 19 Sep to 3 Oct, with 5 work items. The sprint description is: 'Deliver core FastAPI backend setup, SQLite evidence database, and primary metadata parsing modules (URLs, Emails, File hashes) with initial React dashboard...'. The tasks listed are:


Task	Status	Estimate	Assignee
PF-1 Set up FastAPI backend & SQLite evidence database sc...	Done	5	[User]
PF-2 Build URL & Domain metadata extraction API endpoint	In Progress	8	[User]
PF-3 Implement Email header & EML file parser	In Progress	8	[User]
PF-4 Build Browser History & File hash analysis module	To Do	5	[User]
PF-5 Create React evidence upload & scan dashboard	To Do	5	[User]

Below the sprint, there is a 'Backlog' section with 5 work items, a total of 18, and a 'Create sprint' button.

The screenshot shows the Jira Project Foresight interface. The left sidebar contains navigation options: For you, Recent, Starred, Apps, Plans, Spaces, Recent, Project Foresight, AI Customer Support, More spaces, Recommended, Collect requests, Filters, Dashboards, Confluence, and Assets. The main content area displays the 'Project Foresight' space with a 'Backlog' view. A 'Backlog' section is active, showing 5 work items, a total of 18, and a 'Create sprint' button. The tasks listed are:

Task	Status	Estimate	Assignee
PF-6 Develop Search & Evidence Filter UI	To Do	5	[User]
PF-7 Implement Investigator Login & Audit Logging	To Do	3	[User]
PF-8 Accuracy tuning & false-positive reduction testing	To Do	5	[User]
PF-9 Generate PDF Forensic Report Exporter	To Do	3	[User]
PF-10 Final Client Demo & Handoff Documentation	To Do	2	[User]

Below the backlog, there is a '+ Create' button.

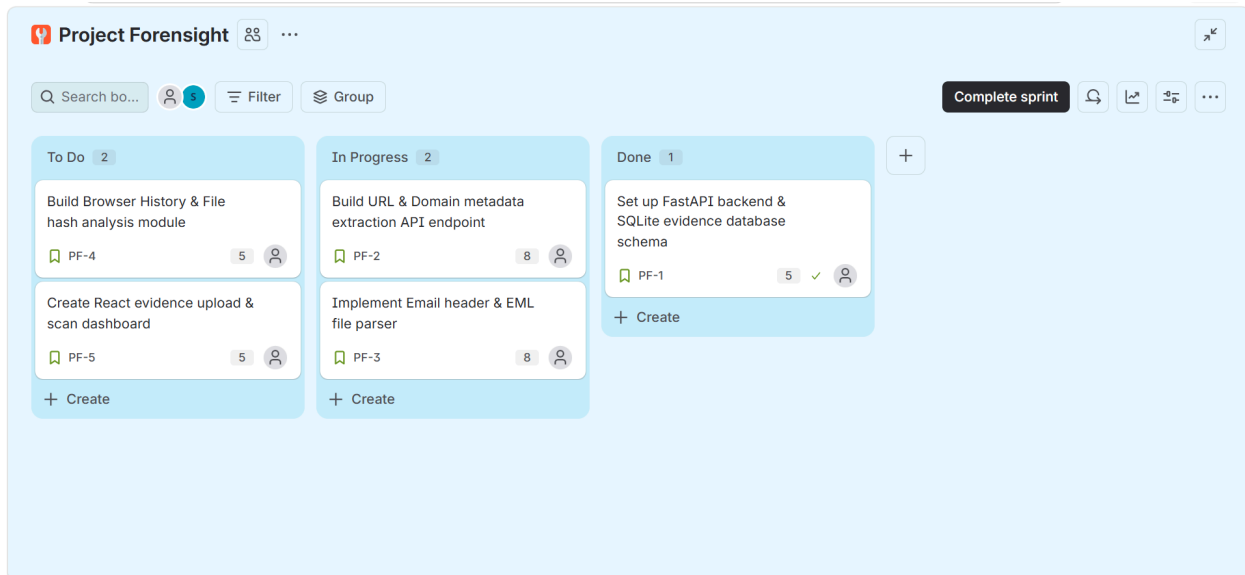

WEEKLY CLIENT STATUS REPORT (TEMPLATE):

SUBJECT: Weekly Project Status Report - Project Foresight (Sprint 3 Update)

Hi Team,

Here is the weekly progress report for Project Foresight. Overall, the project remains ON SCHEDULE and WITHIN BUDGET.

1. EXECUTIVE SUMMARY:

- Health Status: GREEN (On Track)
- Current Milestone: Backend Evidence Extraction Engine (85% Complete)

2. KEY ACCOMPLISHMENTS THIS WEEK:

- Completed FastAPI endpoints for URL and Email header extraction.
- Created SQLite database schema for encrypted evidence storage.
- Conducted Sprint 3 review with the development team.

3. UPCOMING FOCUS FOR NEXT WEEK:

- Complete browser history file extraction logic.
- Begin React frontend dashboard wireframe integration.

4. RISKS & IMPEDIMENTS:

- Identified potential false-positive scoring issues with complex file headers.

- Mitigation: Backend team is refining scoring logic during Sprint 5 QA phase.

Please let me know if you have any questions or feedback.

Best regards,

Project Manager
